


# How many Carpenters and Laborers will I need in the next 3 weeks?

Display: Quantity

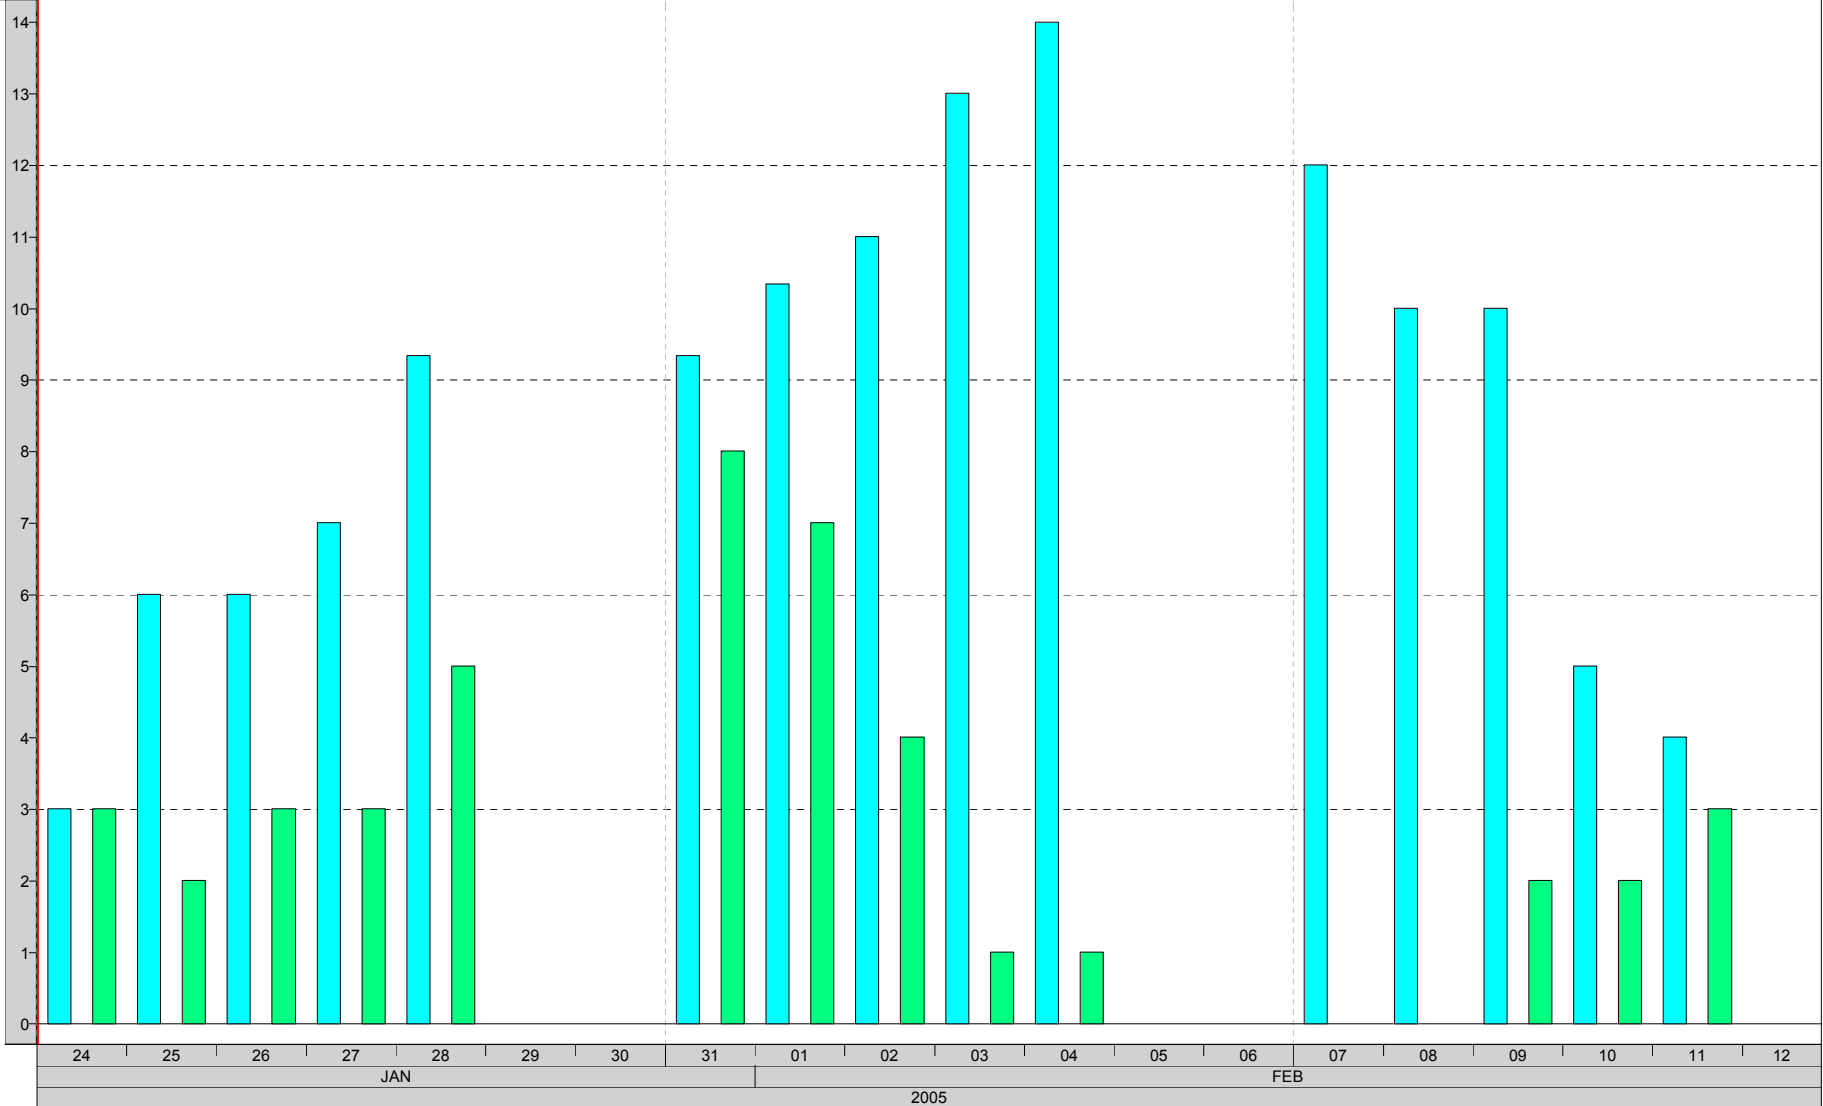

On Feb 3 & 4, I need additional Carpenters and less Laborers. To resolve, I can look at Carpenter activities and have Laborers assist or look at the Total Float for activities that can be delayed.

**Scheduling and Information Services** [www.1sis.com](http://www.1sis.com)  
**Arrow Construction Company**

CAR █  
 LAB █  
 Calculate: Average  
 Display: Quantity  
 Interval: Day



## How many Carpenters and Laborers will I need in the next 3 weeks?

Act ID	Activity Description	Orig Dur	Craft Description	# of Men	Early Start	Early Finish	Total Float	2005			
								JAN		FEB	
								24	31	07	14
AT1310	Hang Kitchen Entry Door ATTL	1	Laborer	1	02/01/05	02/01/05	17d	▲▼ Hang Kitchen Entry Door ATTL			
ST1020	Install Milled Woodwork STEV	5	Carpenters	1	02/01/05	02/07/05	17d	▲▼ Install Milled Woodwork STEV			
HD1020	Install Milled Woodwork HOOD	5	Carpenters	1	02/01/05	02/07/05	22d	▲▼ Install Milled Woodwork HOOD			
CU090	Install Gypsum Wallboard CUM	2	Laborer	2	02/01/05	02/02/05	30d	▲▼ Install Gypsum Wallboard CUM			
CA1180	Install Decking CAR	4	Carpenters	2	02/02/05	02/07/05	5d	▲▼ Install Decking CAR			
ST1130	Install Faucet and Fixtures STEV	1	Laborer	1	02/02/05	02/02/05	20d	▲▼ Install Faucet and Fixtures STEV			
HD1130	Install Faucet and Fixtures HOOD	1	Laborer	1	02/02/05	02/02/05	25d	▲▼ Install Faucet and Fixtures HOOD			
CU070	Install Door Frame CUM	1	Carpenters	1	02/02/05	02/02/05	33d	▲▼ Install Door Frame CUM			
HL300	Install Cabinets HILL	5	Carpenters	2	02/03/05	02/09/05	3d	▲▼ Install Cabinets HILL			
RI1090	Install Gypsum Wallboard RIV	2	Laborer	1	02/03/05	02/04/05	3d	▲▼ Install Gypsum Wallboard RIV			
BE1230	Install Tiki Bar roof post, joists, beams	3	Carpenters	3	02/03/05	02/07/05	5d	▲▼ Install Tiki Bar roof post, joists, beams CAR			
HL130	Install Island HILL	2	Carpenters	2	02/03/05	02/04/05	6d	▲▼ Install Island HILL			
AT1020	Install Milled Woodwork ATTL	5	Carpenters	1	02/04/05	02/10/05	10d	▲▼ Install Milled Woodwork ATTL			
CU170	Install Pantry with shelving CUM	4	Carpenters	1	02/04/05	02/09/05	25d	▲▼ Install Pantry with shelving CUM			
02/07/05											
BE1240	Install Tiki Bar roof CAR	2	Carpenters	3	02/08/05	02/09/05	5d	▲▼ Install Tiki Bar roof CAR			
CA1230	Install Tiki Bar roof post, joists, beams	3	Carpenters	2	02/08/05	02/10/05	5d	▲▼ Install Tiki Bar roof post, joists, beams CAR			
RI1010	Install Finish Carpentry RIV	5	Carpenters	1	02/08/05	02/14/05	17d	▲▼ Install Finish Carpentry RIV			
ST1110	Install Toilet STEV	1	Laborer	1	02/09/05	02/09/05	15d	▲▼ Install Toilet STEV			
HD1110	Install Toilet HOOD	1	Laborer	1	02/09/05	02/09/05	20d	▲▼ Install Toilet HOOD			
BE1300	Install Stairs CAR	3	Carpenters	1	02/10/05	02/14/05	5d	▲▼ Install Stairs CAR			
RUM106	Remove old appliances RUM	2	Laborer	2	02/10/05	02/11/05	15d	▲▼ Remove old appliances RUM			
RI1190	Install Sinks RIV	1	Laborer	1	02/11/05	02/11/05	3d	▲▼ Install Sinks RIV			
CA1240	Install Tiki Bar roof CAR	3	Carpenters	2	02/11/05	02/15/05	5d	▲▼ Install Tiki Bar roof CAR			
02/14/05											
RI1150	Install Steam Shower RIV	1	Laborer	2	02/14/05	02/14/05	3d	▲▼ Install Steam Shower RIV			
ST1170	Install Heated Towel Rack STEV	1	Laborer	1	02/14/05	02/14/05	3d	▲▼ Install Heated Towel Rack STEV			
HD1170	Install Heated Towel Rack HOOD	1	Laborer	1	02/14/05	02/14/05	8d	▲▼ Install Heated Towel Rack HOOD			
RUM124	Remove old cabinets RUM	2	Laborer	2	02/14/05	02/15/05	15d	▲▼ Remove old cabinets RUM			
HL190	Install Sinks HILL	1	Laborer	1	02/14/05	02/14/05	27d	▲▼ Install Sinks HILL			


On Feb 3 & 4, I need additional Carpenters and less Laborers. To resolve, I can look at Carpenter activities and have Laborers assist or look at the Total Float for activities that can be delayed.

**Scheduling and Information Services**  
**Arrow Construction Company**

CAR ■  
LAB ■  
Calculate: Average  
Display: Quantity  
Interval: Day

# How many Carpenters and Laborers will I need in the next 3 weeks?

Display: Quantity

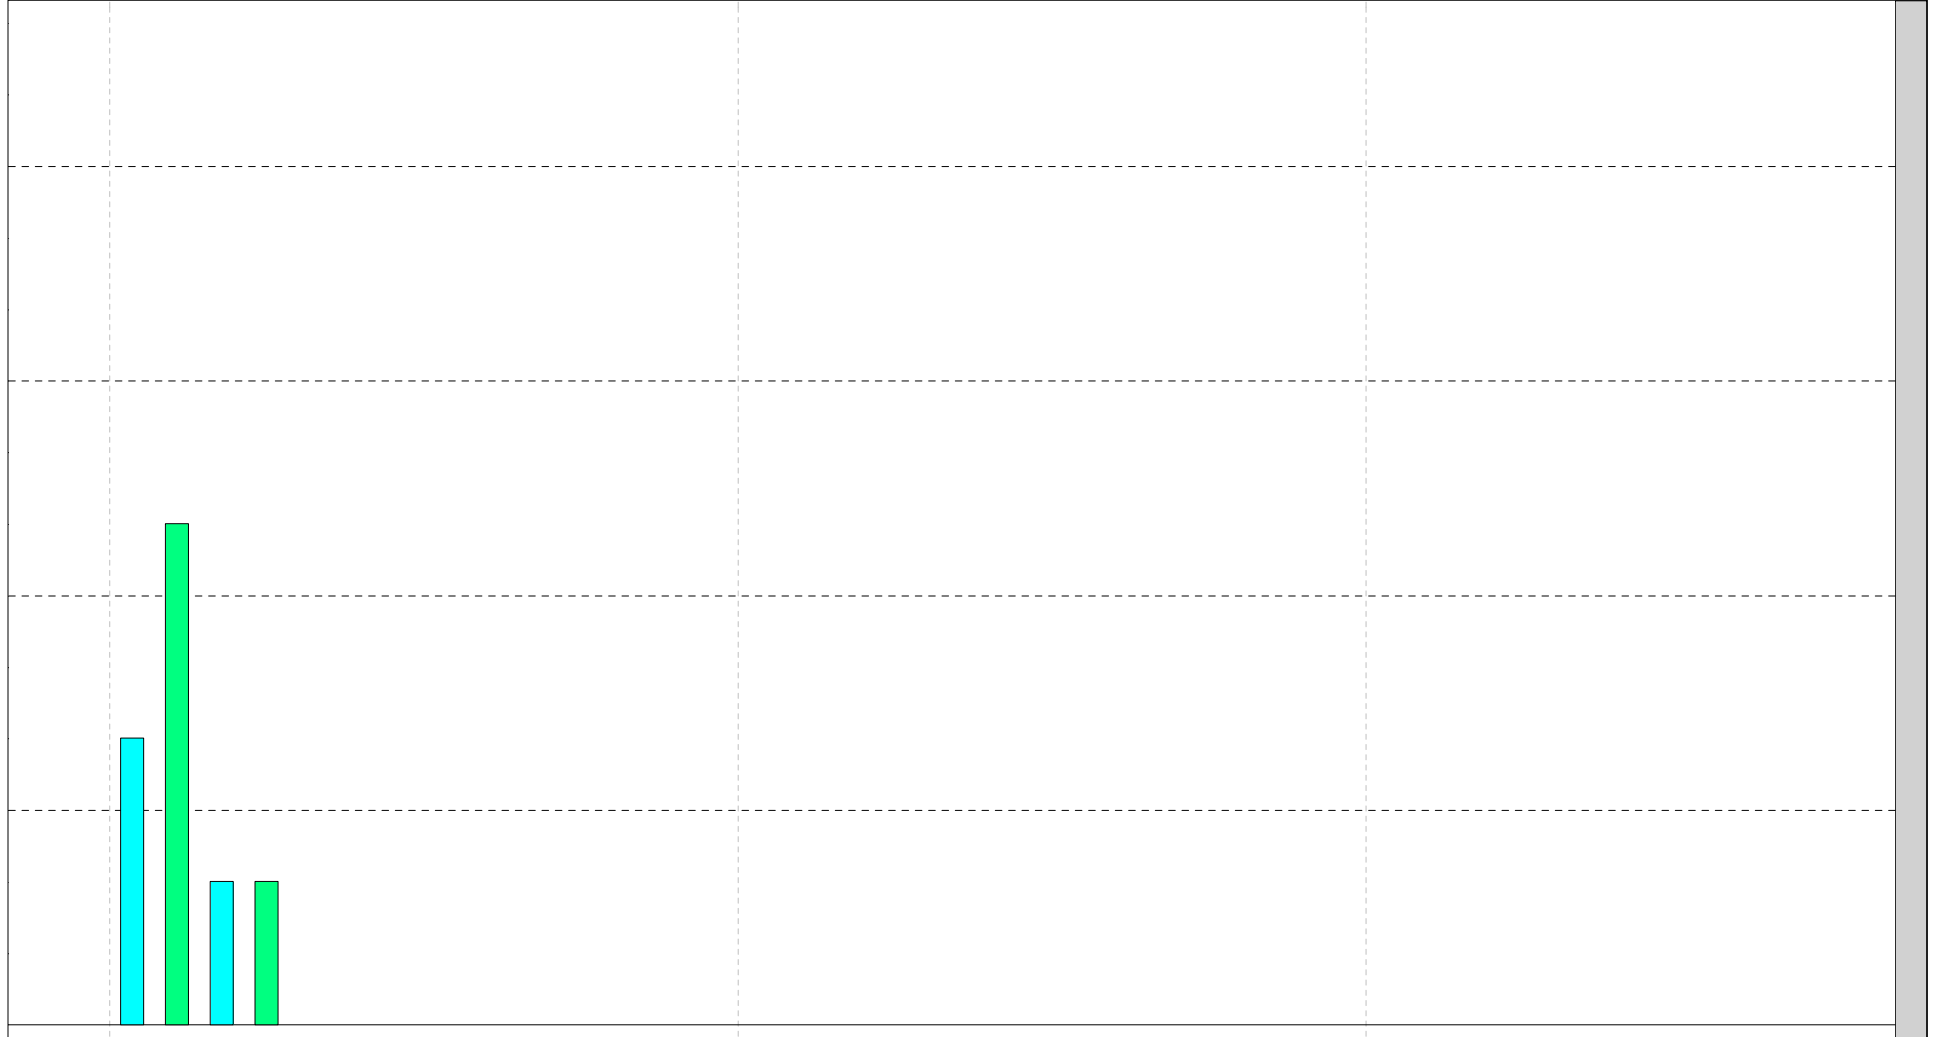

13 14 15 16 17 18 19 20 21 22 23 24 25 26 27 28 01 02 03 04 05 06  
 FEB 2005 MAR

On Feb 3 & 4, I need additional Carpenters and less Laborers.  
 To resolve, I can look at Carpenter activities and have Laborers assist or look at the Total Float for activities that can be delayed.

**Scheduling and Information Services**  
**Arrow Construction Company**

CAR █  
 LAB █  
 Calculate: Average  
 Display: Quantity  
 Interval: Day

## How many Carpenters and Laborers will I need in the next 3 weeks?

ID	Display: Quantity																			
CAR	3	6	6	7	9			9	10	11	13	14			12	10	10	5	4	
LAB	3	2	3	3	5			8	7	4	1	1					2	2	3	
	24	25	26	27	28	29	30	31	01	02	03	04	05	06	07	08	09	10	11	12
	JAN									FEB										
	2005																			


On Feb 3 & 4, I need additional Carpenters and less Laborers.  
To resolve, I can look at Carpenter activities and have Laborers assist or look at the Total Float for activities that can be delayed.

**Scheduling and Information Services**  
**Arrow Construction Company**

CAR ■ —  
 LAB ■ —  
 Calculate: Average  
 Display: Quantity  
 Interval: Day

## How many Carpenters and Laborers will I need in the next 3 weeks?

Display: Quantity																					
		4	2																		
		7	2																		
13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	01	02	03	04	05	06
FEB													MAR								
2005																					



On Feb 3 & 4, I need additional Carpenters and less Laborers.  
 To resolve, I can look at Carpenter activities and have Laborers assist or look at the Total Float for activities that can be delayed.

**Scheduling and Information Services**  
**Arrow Construction Company**

CAR █ —  
 LAB █ —  
 Calculate: Average  
 Display: Quantity  
 Interval: Day
